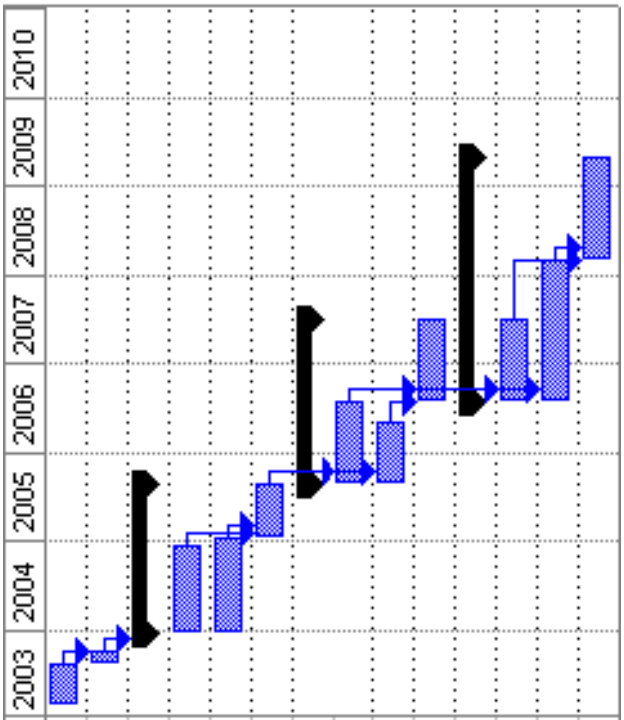ID	Task Name	Duration
1	Public Input on Alternatives	6 mons
2	Selection of Preferred Alternative	2 mons
3	**PUC Approval on Phases 1 & 2**	**22 mons**
4	Information Requests of HECO	13 mons
5	Environmental Assessment	14 mons
6	Complete PUC Proceeding	8 mons
7	**Ph. 1 - Kamoku 46kV Alternative**	**24 mons**
8	Ph. 1 - Detailed Design/Material Procurement	12 mons
9	Ph. 1 - Permit Drawings/Permit Acquisition	9 mons
10	Ph. 1 - Construction	12 mons
11	**Ph. 2 - Archer Tsf/King St. 46kV UG Lines**	**36 mons**
12	Ph. 2 - Detailed Design/Material Procurement	12 mons
13	Ph. 2 - Permit Drawings/Permit Acquisition	21 mons
14	Ph. 2 - Construction	15 mons
